MELROSE TWP SEWER EXPANSION

Project Schedule

Preparation Date: 6/1/2026

Project Start: Sat, 6/1/2024

Display Week: 1
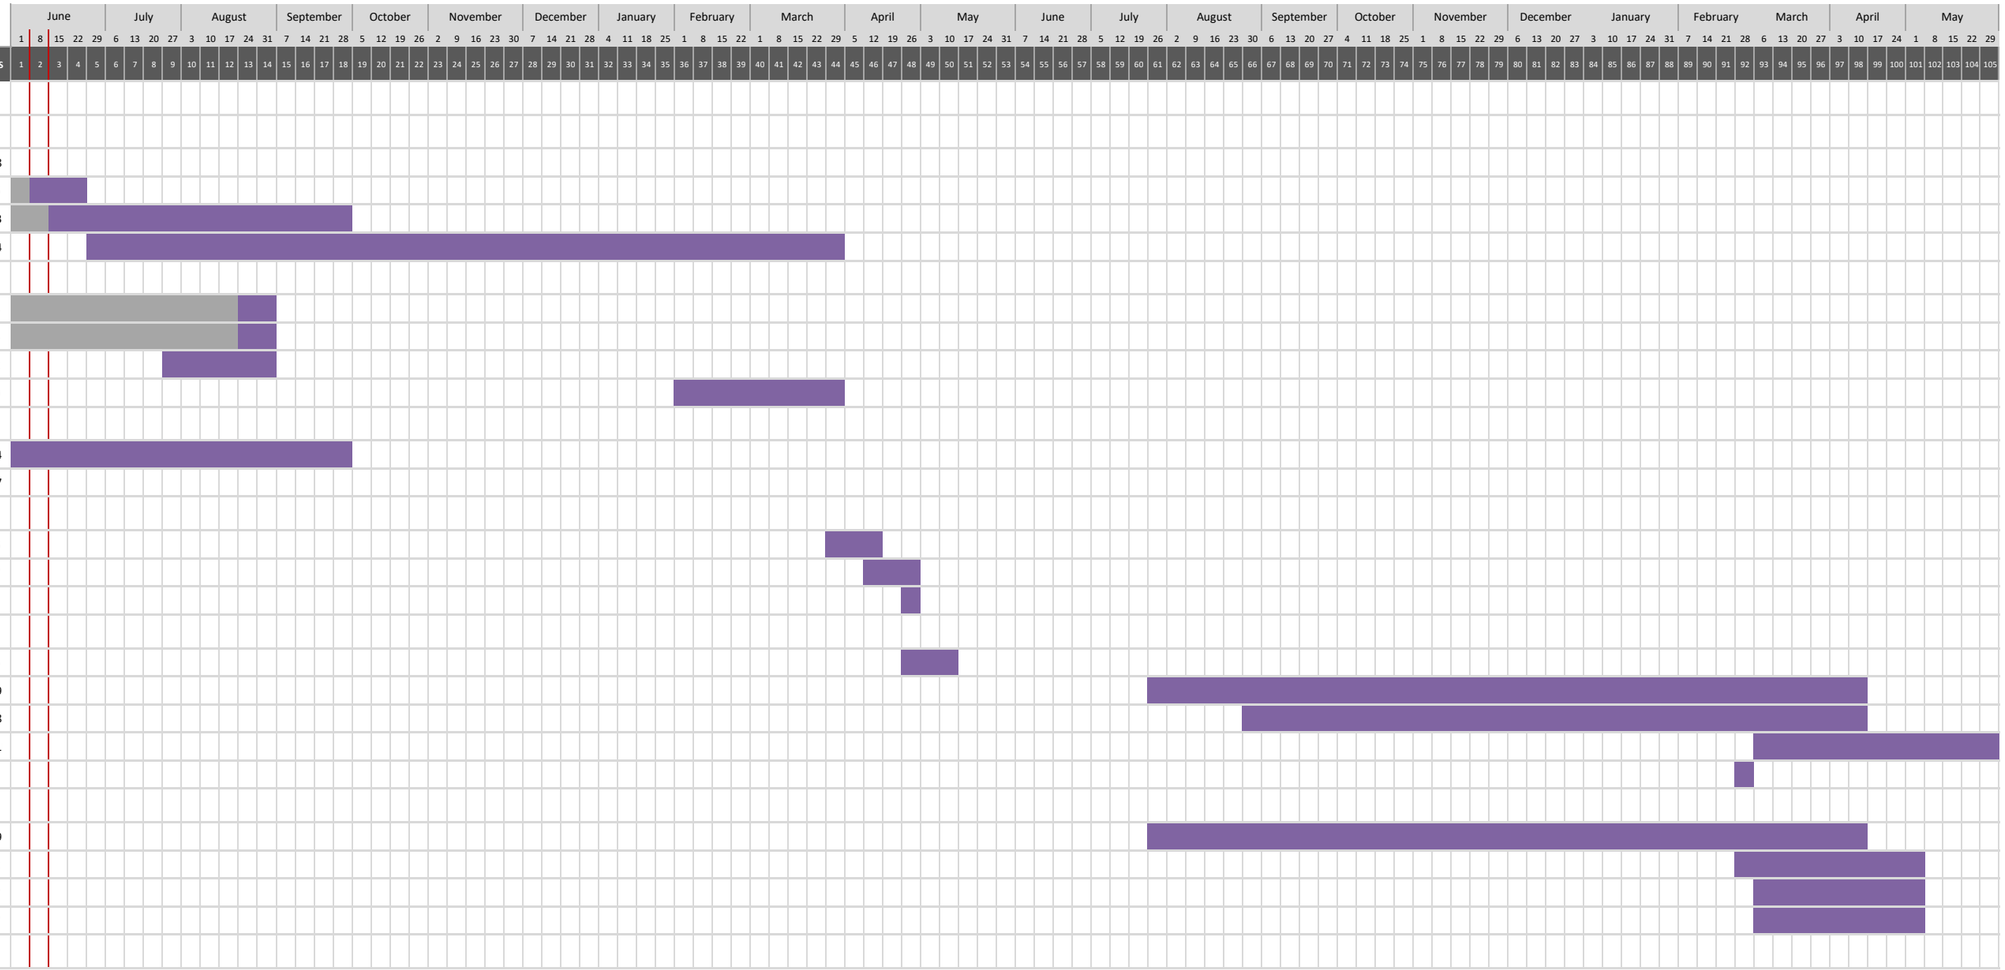
TASK	PROGRESS	START	END	DAYS
Administration				
PER Preparation	100%	6/1/25	3/15/26	288
USDA Pre-Application Review	10%	6/1/26	6/26/26	26
Public Outreach & Twp Review	10%	6/1/26	10/1/26	123
Funding Approval	0%	7/1/26	3/31/27	274
Design Development				
Drawing Preparation	85%	6/1/26	9/1/26	93
Specification Preparation	85%	6/1/26	9/1/26	93
Owner Review	0%	8/1/26	9/1/26	32
Bid Document Preparation	0%	2/1/27	3/31/27	59
Permitting				
EGLE Part 41	15%	4/1/26	10/1/26	184
EGLE NPDES Permitting	100%	5/1/25	2/1/26	277
Bidding & Award				
Bid Solicitation	0%	3/31/27	4/15/27	16
Bid Review and Approval	0%	4/15/27	5/1/27	17
Contract Award	0%	5/1/27	5/1/27	1
Construction				
Pre-Costruction Sumbittals	0%	5/1/27	5/15/27	15
WWTF Upgrades	0%	8/1/27	4/15/28	259
Force Main Construction	0%	9/1/27	4/15/28	228
Lateral Construction and LPS Installs	0%	4/15/28	4/15/30	731
Substantial Completion	0%	3/1/28	3/1/28	1
Project Administration				
Engineering Inspections - Periodic	0%	8/1/27	4/15/28	259
Engineer Certification & As-Built Dwgs	0%	3/1/28	5/1/28	62
Permit Closeouts	0%	4/15/28	5/1/28	17
Project Closeout	0%	4/15/28	5/1/28	17
